

Gas Interconnector Bulgaria – Serbia (IBS) Serbian Section Progress Report

Project Implementation Unit



Gas Interconnector Bulgaria – Serbia (IBS) Serbian Section Progress Report


Project Implementation Unit

IBS Serbian section – in Brief

Pipeline length	108km
Pipeline Diameter	DN700
Commission year	May 2022
Investment cost	85.5 M €

Project Status:

- FS and CBA implemented.
- Spatial Plan of Special Purpose completed.
- Geo exploration works completed.
- Technical design completed.
- Construction Permit obtained.
- Land expropriation in progress.
- Construction Works Tender Dossier preparation in progress.

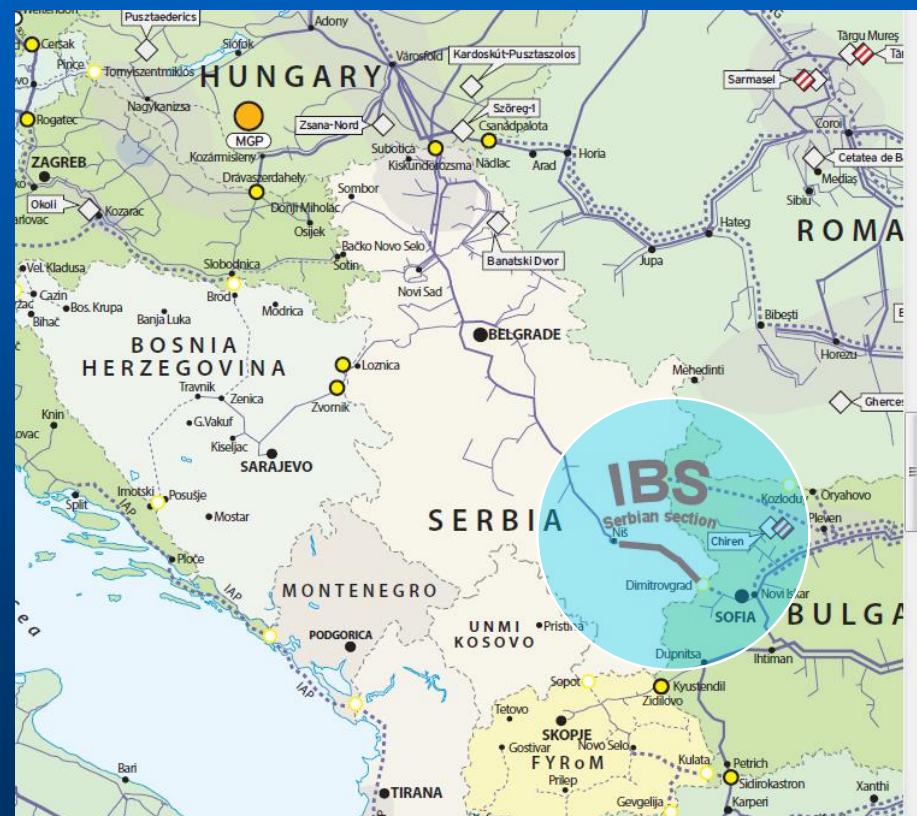

Gas Interconnector Bulgaria – Serbia (IBS) Serbian Section Progress Report

Project Implementation Unit

Project Implementation Key Remarks and Milestones

Project Owner - Ministry of Mine and Energy of the Republic of Serbia
Project Beneficiary - PE SRBIJAGAS - > TRANSGAS

PE SRBIJAGAS Project Implementation Activities Framework:

- Conclusion of June 2017 by which the Government of Serbia agreed that PE Srbijagas, on behalf of and for the account of the Republic of Serbia, undertakes all necessary activities for the purpose of resolving of property and legal issues on the route of the natural gas transmission system Nis - Dimitrovgrad - the border of the Republic of Serbia and the Republic of Bulgaria (MG-10), as an integral part of the gas interconnection Republic of Serbia - Republic of Bulgaria
- Conclusion of January 2018, by which the Government of Serbia agreed that PE Srbijagas undertakes the necessary activities in order to develop design and technical documentation by August 2019.

Gas Interconnector Bulgaria – Serbia (IBS) Serbian Section Progress Report


Project Implementation Unit

Project Implementation Key Remarks and Milestones

Project Implementation Status Report and Milestones:

- **Technical design** completed. Respecting the importance to follow up timeframe deadlines regarding construction works contracting mechanism under the IPA 2017, PE Srbijagas delivered the Technical design documentation, including Construction Permit as planned.
- **Technical Tender Dossier** documentation delivered to Consultant responsible for Construction Works Tender Dossier preparation – CONNECTA.

Construction Works Tendering Timeline :

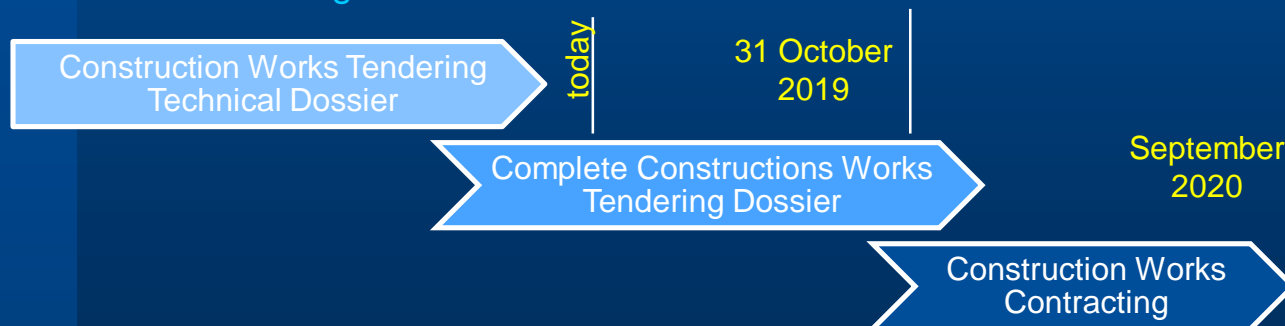

Gas Interconnector Bulgaria – Serbia (IBS) Serbian Section Progress Report

Project Implementation Unit

Project Implementation Key Remarks and Milestones

Project Implementation Status Report and Milestones:

- **Status of Resolving property and legal issues** on the gas pipeline route:

The court experts completed the field task on the route of the gas pipeline and provided all the findings / assessments - for 4584 cadastral lots, on the territory of Dimitrovgrad, Bela Palanka, Pirot and Niš. Offers for compensation for damage to each owner of real estate are continuously being submitted to the relevant municipal administrations.

**Thank you
for your attention**



СРБИЈАГАС

IBS Serbian Section PIU
