

New Interconnectors between Hungary and Slovakia (PCI 3.16, PCI 3.17)

CESEC Electricity Plenary and Working Group Meeting
9th October 2019, Brussels

Gönyű-National Border (Gabcikovo, Velky Dur) 400 kV (PCI 3.16)



Information on the implementation of the PCI 3.16 – Hungarian part

✓ Final right-of-way permissions - 31/07/2019 and 13/08/2019

Next steps

- Public procurement processes from 2019 Q4
- Start of construction for OHL 2019 Q4
- Start of construction for substation 2020 Q1
- Finishing construction works 2020 Q4
- Commissioning December 2020


Challenges

- Additional activities (change of bay order of existing OHLs, cutting and replanting forest etc.)
- Additional tasks (questions of forest area, gas pipeline, industrial zone etc.)
- Public procurement - risk of delay



*EU contribution:
139 033.89 EUR for preparation works
Close of action 12/2018*

Information on the implementation of the PCI 3.16 – Slovak part

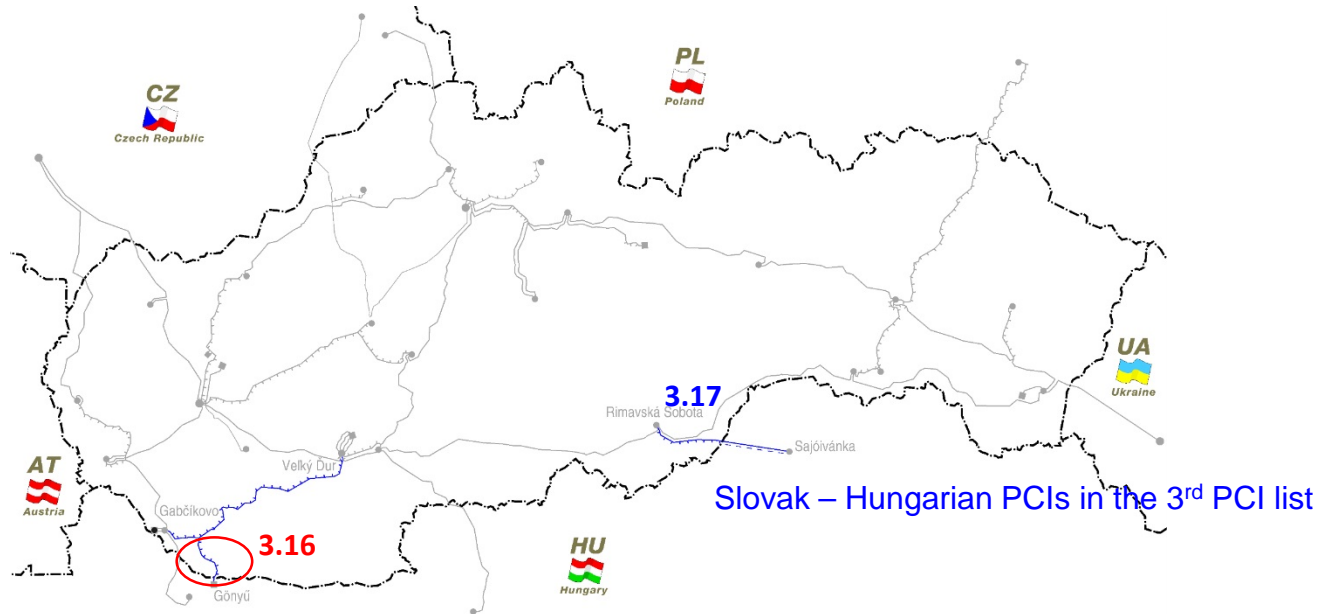



Progress in implementation

- Tendering process for project constructors ► **ON GOING** (signing the contract with constructor by end of October 2019)

Next steps

- Beginning of building works in November 2019
- Commissioning by December 2020

Sajóivánka-National Border (Rimavská Sobota) 400 kV (PCI 3.17)

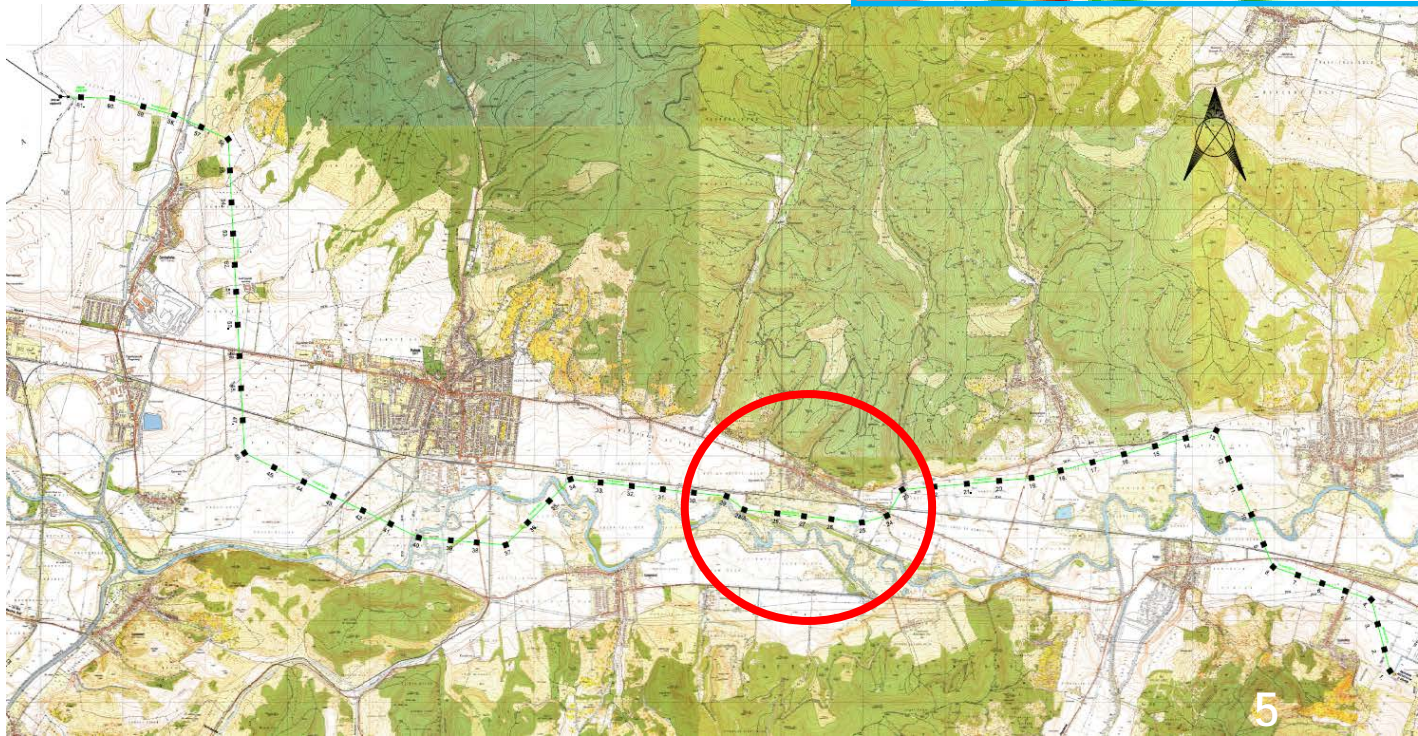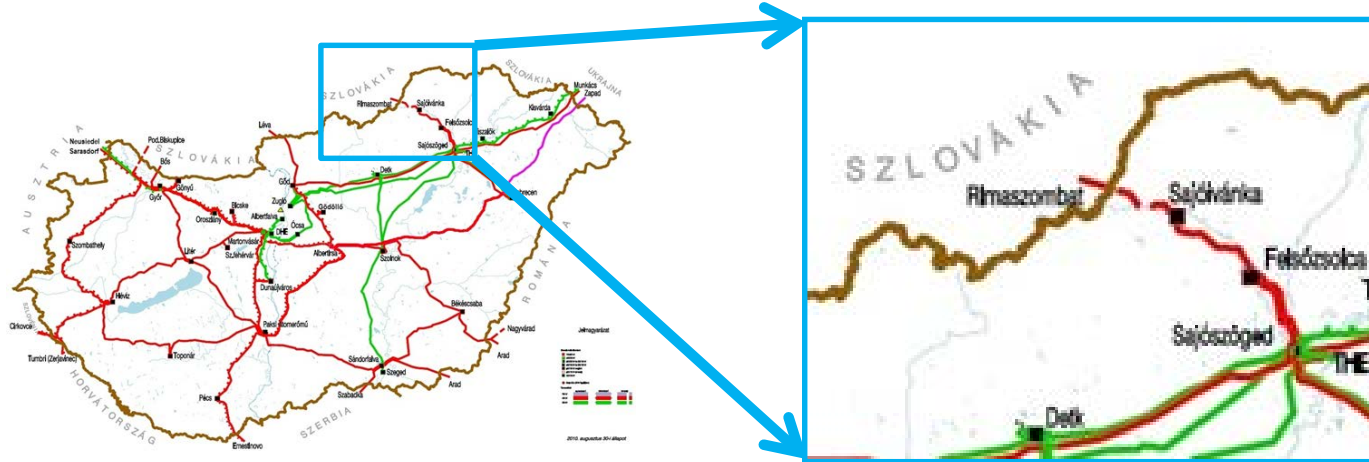

Information on the implementation of the PCI 3.17 – Hungarian part

✓ Right-of-way permission - 16/08/2019

Next steps

- Public procurement processes from 2019 Q4
- Start of construction for OHL 2019 Q4
- Start of construction for substation 2020 Q1
- Finishing construction works 2020 Q4
- Commissioning December 2020


Challenges

- Public procurement – risk of delay
- Correct contact with landowners during construction works (well prepared process – appropriate compensation)



EU contribution
111 517 EUR for preparation works
Close of action 04/2018

Information on the implementation of the PCI 3.17 – Slovak part

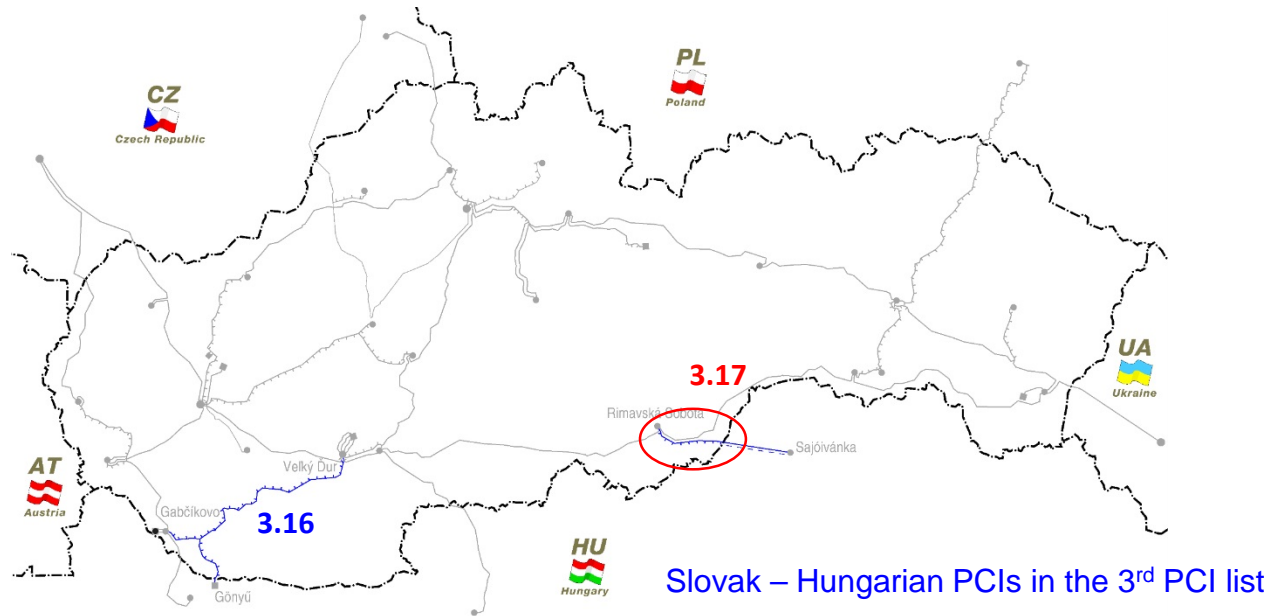

Progress in implementation

- Signing the contract with project constructor in July 2019
- Beginning of building works in August 2019

Next step

- Commissioning by December 2020

New Interconnectors between Hungary and Slovakia (PCI 3.16, PCI 3.17)

Thank you for your attention!
